Gantt Chart

Project: Document Management System (DMS)

Task 2 - Project Planning

Prepared by	Role
Omar Ayman Shebl Motawea	Project Manager / Business Analyst
Michael Erian Ayad Sadhom	System Designer / UI/UX Designer
Gamal Hamed Gamal Aldin	Documentation & QA

1. Schedule Breakdown and Task Timelines

The table and chart below show the schedule of the planning phase of the Document Management System. Times are in working days counted from day 0.

Activity	Predecessors	Duration	Timeline (days)
A: System Request Formulation	-	2 days	Day 0 to day 2
B: Feasibility Study (Economic & Technical)	-	4 days	Day 0 to day 4
C: Methodology Selection & Documentation	B	5 days	Day 4 to day 9
D: Time Estimation & Scheduling	A, C	3 days	Day 9 to day 12

2. Gantt Chart

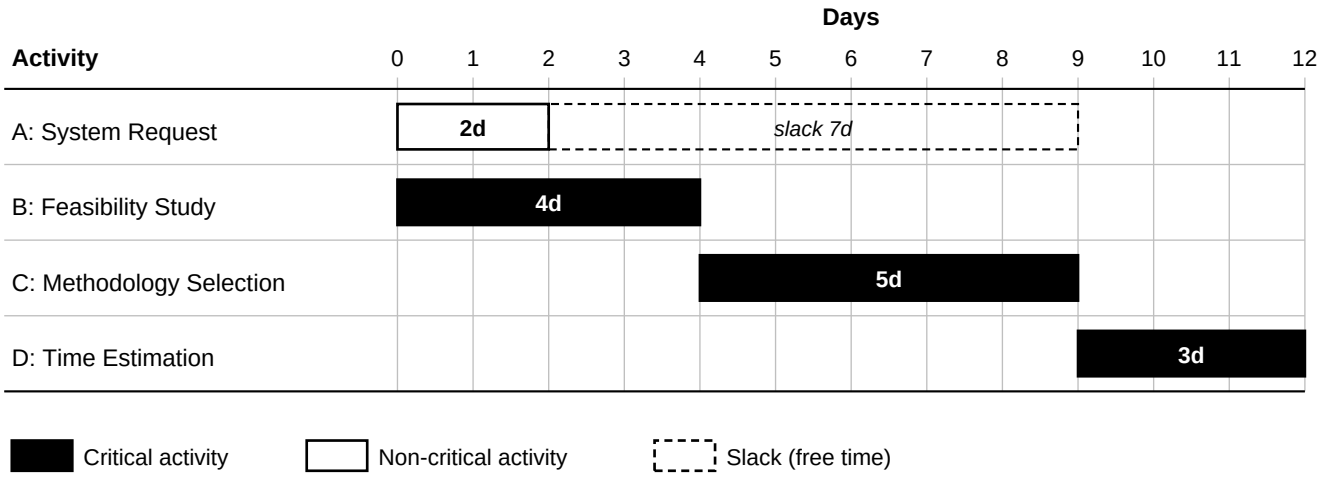

Gantt chart of the planning phase (12 working days).

3. Schedule Observations

- Activities A and B start together on day 0, so the team writes the system request and studies feasibility at the same time.
- Activity C (methodology) starts when B finishes on day 4, because the choice of methodology uses the feasibility results.
- Activity D (time estimation and scheduling) starts on day 9, when both A and C are finished, and ends on day 12.

- Activity A finishes on day 2 but is not needed until day 9, so it has 7 days of slack.

4. Critical Path

The critical path is **B - C - D** (4 + 5 + 3 = 12 days). A delay in any of these activities delays the end of the planning phase. The team adds a one-day buffer, so the target finish is day 13.

5. Responsibilities

Activity	Responsible	Reviewer
A: System Request	Omar	Gamal
B: Feasibility Study	Omar	Gamal
C: Methodology	Omar	Michael
D: Time Estimation	Omar	Gamal

The schedule is tracked on the Trello board. Each card has a due date that follows the dates in this chart, and the Project Manager checks planned versus actual progress at the weekly meeting.

6. Link with the Whole Project

This chart covers the planning activities only. The full project follows the 11-week work plan of Lab 6, where the weekly timeline continues with requirements, DFD, UML, UI design and final documentation.
