PERT Chart

Project: Document Management System (DMS)

Task 2 - Project Planning

Prepared by	Role
Omar Ayman Shebl Motawea	Project Manager / Business Analyst
Michael Erian Ayad Sadhom	System Designer / UI/UX Designer
Gamal Hamed Gamal Aldin	Documentation & QA

1. Purpose

The PERT chart shows the order of the planning activities, which activity must finish before another can start, and which path decides the total project time.

2. Activities

Code	Activity	Predecessors	Duration (days)
A	System Request Formulation	-	2
B	Feasibility Study (Economic & Technical)	-	4
C	Methodology Selection & Documentation	B	5
D	Time Estimation & Scheduling	A, C	3

3. PERT Network Diagram

Each box is an activity with its duration. Arrows show the order of work. The thick line is the critical path.

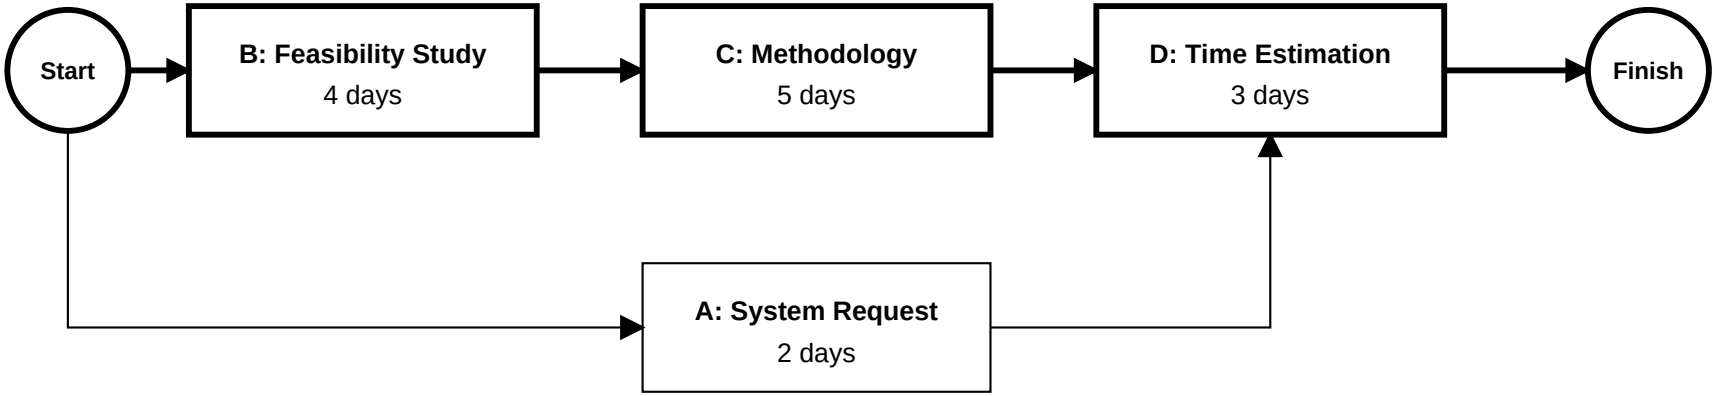

PERT network of the planning activities.

4. Paths and Critical Path

A path is a chain of activities from Start to Finish. The longest path decides the total time.

Path	Calculation	Length
A, D	2 + 3	5 days
B, C, D (critical path)	4 + 5 + 3	**12 days**

The critical path is **B - C - D** and the project takes **12 days**. A delay in any critical activity delays the whole project.

Activity A is not on the critical path. Path A, D is 5 days, 7 days shorter than the critical path, so A can be delayed up to **7 days** without delaying the project.

5. Conclusion

Feasibility (B), methodology (C) and time estimation (D) control the schedule, so the Project Manager should watch them closely every week.
